

6 Premier Drive, Albion Park NSW 2527
Telephone: 0242574770
Mobile No: 0418 471 343

Email: jonspin@bigpond.com.au

HAZARDOUS MATERIALS ASSESSMENT REPORT

Client: Cape Cod Australia Pty. Limited

Job details: Owner/s: Mr. M. Bicknell & Ms. F. Cattell

Location: 66 Plowman Street, North Bondi

Plans for Job No: 7592/14 Revision No: D Dated: 25-11-14

Council area: WAVERLEY

Date of assessment: 11th December 2014

Our reference: HM03561214


The Client acknowledges that:

This report is provided for **the exclusive information of the Client**. It is a term and condition of the terms upon which this report is provided, that if the Client chooses to rely upon the report, that the Company and the Person making this report will not be liable to the Client or to any other Person who suffers personal or property damage or financial loss in respect of any cause of action or tort, contract or however the cause of action is said to arise.

This report is **not a guarantee or warranty** or an all-encompassing report dealing with the above property from every aspect. It is based on the condition of the property and the "**Readily Accessible Areas**" at the time of assessment. It is a reasonable attempt to identify as far as *reasonably practicable*, any significant hazardous materials i.e. materials "that may" contain asbestos [ACM] or [ACD], ceiling dusts "that may" contain lead, paints "that may" contain lead or synthetic mineral fibres [SMF], **visible** at the time of assessment.

This report, based on visual assessment, will not disclose hazardous materials in inaccessible areas, not readily accessible or obstructed at the time of assessment. Areas which are not normally accessible were not assessed and include but are not limited to – inside walls, the interior of a flat roof or beneath a suspended floor filled with earth.

This report is **not a Certificate of Compliance** with the requirements of the WHS Act 2011 and WHS Regulations 2011, relevant Codes of Practice or Australian Standards or NSW Office of Environment and Heritage [OEH] Regulations.

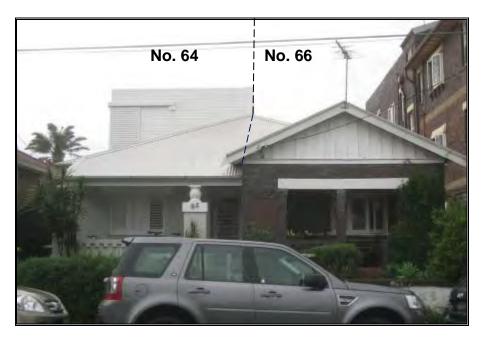

Front north western elevation of the adjoining properties: No. 64 & No. 66 Plowman Street, North Bondi

1. GENERAL DESCRIPTION OF THE EXISTING RESIDENCE

Estimated age:	Circa 1920-1930					
Type of construction:	Semi detached single storey full brick/ brick cavity construction on a combination of sandstone block footings and brick piers supporting a suspended timber floor system.					
External cladding:	ay masonry brickwork					
Roof:	Common traditional cut and pitched hipped and valley structure with front gable.					
	The street elevation section of roof is decked with pre-finished corrugated profile sheet metal roofing.					
	The main roof surface is terra cotta roofing tiles.					

Occupancy Status: Was the residence occupied at the time of assessment?

Yes	✓	No		Not Applicable	
-----	---	----	--	----------------	--

Orientation: For the purpose of this report the front of the residence faces:

						,	.		ı
East	West	North	South	Northeast	Northwest	✓	Southeast	Southwest	1
									i

2. AREAS ASSESSED

This assessment covers the following "Readily Accessible Areas" of the existing residence layout to identify as far as reasonably practicable any significant hazardous materials i.e. materials "that may" contain asbestos [ACM] or [ACD], ceiling dusts "that may" contain lead, paints "that may" contain lead or synthetic mineral fibre insulation [SMF].

Under Floor Space	N/A	Exterior	✓	Roof Surfaces	✓	Roof Cavity	✓	Interior	✓	Carport	N/A	
-------------------	-----	----------	---	---------------	---	-------------	---	----------	---	---------	-----	--

3. ASSESSMENT OF THE EXISTING RESIDENCE LAYOUT FOR HAZARDOUS MATERIALS

Area Assessed	Description and Comment	Assessment / Action				
Under Floor Space	No access is available to the underfloor area. Note: no work is proposed in the underfloor area as part of the proposed Contract works.	No action is required.				
Exterior						
Cladding	Clay masonry brickwork	Appropriate dust suppression measures to be provided. No further action is required.				
	Vertical timber weatherboards to the front gable. Note: not associated with the proposed Contract works.	No action is required.				
Eave soffit lining	Timber lining boards to top of exposed rafters to the southwest elevation. Note: eaves to be demolished to accommodate first floor frame as part of the proposed Contract works.	Appropriate dust suppression measures to be provided. No further action is required.				
	Timber lining boards to the front gable soffit Note: not associated with the proposed Contract works.	No action is required.				
Roofing	Pre-finished corrugated profile sheet metal roofing to the street elevation section of common roof. Note: roof structure to be partially removed to accommodate first floor frame as part of the proposed Contract works.	Appropriate dust suppression measures to be provided. No further action is required.				
	Terra cotta roofing tiles to the main roof pitched roof and rear skillion section. Note: roof structure to be removed to accommodate first floor frame as part of the proposed Contract works.					
Front patio	Possible asbestos cement [ACM] sheet with timber cover battens to the patio soffit. Note: not associated with the proposed Contract works.	All necessary steps are to be taken to protect the possible AC soffit lining from damage during the course of the works.				
Rear patio / deck	Ground level timber deck structure. Note: deck structure to be removed to accommodate proposed brick veneer addition as part of the proposed Contract works.	Appropriate dust suppression measures to be provided. No further action is required.				

Area Assessed	Description and Comment	Assessment / Action
Painting - general	Combination of oil based and acrylic based surface coating to timber windows, eaves, fascia and trims. No exposed lead based paints were observed.	Appropriate dust suppression measures to be provided. No further action is required.
Interior		
Entry / Hallway	Painted cement render to the walls. Decorative fibrous plaster ceiling with decorative profile plaster cornices. Note: not associated with the proposed Contract works.	No action is required.
Bedroom 1 Note: Shown as Bedroom 3 on Construction Drawing 3 of 8 for Job No. 7592/14	Painted cement render to the walls. Decorative fibrous plaster ceiling with decorative profile plaster cornices. Note: not associated with the proposed Contract works.	No action is required.
Bedroom 2 Note: Shown as Bedroom 4 on Construction Drawing 3 of 8 for Job No. 7592/14	Painted cement render to the walls. Decorative fibrous plaster ceiling with decorative profile plaster cornices. Note: not associated with the proposed Contract works.	No action is required.
Bathroom Note 1: roof space access Note 2: Shown as Shower on Construction Drawing 3 of 8 for Job No. 7592/14	Painted cement render to the walls above wall tiles to 1.2m. Decorative fibrous plaster ceiling with cove profile plaster cornices. Note: opening to be cut in brick external wall and through wall exhaust fan install as part of the proposed Contract works.	Appropriate dust suppression measures to be provided. No further action is required.
Lounge room Note: fireplace.	Painted cement render to the walls. Decorative fibrous plaster ceiling with decorative profile plaster cornices. Note: not associated with the proposed Contract works.	No action is required.

Area Assessed	Description and Comment	Assessment / Action
Kitchen / Family	Combination of painted cement render and plasterboard to the walls. Plasterboard to level section of ceiling with cove profile plaster cornices. Possible asbestos cement [ACM] sheet or soft board with cover battens to the raked ceiling section. Note: bulkhead to be removed raked ceiling to be levelled; ceiling frame adjusted to accommodate internal staircase; new ceiling lining and cornices installed; existing rear wall to be demolished and new brick veneer extension built; walls to be built up as required as part of the proposed Contract works.	9.6m² Remove and dispose of the asbestos cement [ACM] in a manner approved by WorkCover NSW, NSW OEH and Waverley Council. See attached Safe Work Method Statement for the removal of material that may contain asbestos [ACM]. Appropriate dust suppression measures to be provided. No further action is required.
External WC Note: raked ceiling	Face brickwork to the walls. Possible asbestos cement [ACM] sheet to the ceiling. Note: to be completely demolished as part of the proposed Contract works.	1.2m² Remove and dispose of the asbestos cement [ACM] in a manner approved by WorkCover NSW, NSW OEH and Waverley Council. See attached Safe Work Method Statement for the removal of material that may contain asbestos [ACM]. Appropriate dust suppression measures to be provided. No further action is required.
Painting - general	Combination of oil based and acrylic based surface coating to ceilings, walls, doors, windows and trims. No exposed lead based paints were observed.	Appropriate dust suppression measures to be provided. No further action is required.
Pitched Roof Cavity	Common traditional cut and pitched timber roof structure and ceiling frame. Note 1: roof structure to be removed to accommodate first floor frame as part of the proposed Contract works. Note 2: common brick party wall with adjoining property; No. 64 is noted. Note 3: foil back sarking noted to the underside of the sheet metal roofing to the street elevation. No sarking to the underside of the terra cotta tiles. No insulation noted in the ceiling space. Minimal ceiling dust was noted.	In our opinion the air quality will not be generally affected during the course of the construction of the new upper floor frame. Remove and dispose of the sarking in a manner approved by WorkCover NSW, NSW OEH and Waverley Council. Appropriate dust suppression measures to be provided. No further action is required.

Area Assessed	Description and Comment	Assessment / Action	
Skillion Roof Cavity	Inspection of the roof cavity was not carried out due to the method of construction.	Appropriate dust suppression measures to be provided.	
	Note 1: roof structure to be removed and walls built up as part of the proposed Contract works.	No further action is required.	
Electrical Meter Board	Meter board is located on the <i>common</i> privacy wall to the front patio.	No action is required.	
	Note: to be retained in current position as part of the proposed Contract works.		
	a of materials " <i>that may"</i> contain to be removed as part of the proposed	10.8m ²	

DEMOLITION WORK PLAN

The partial demolition of the residence and the removal, storage, handling and disposal of building materials must be carried out as far as *reasonably practicable* in accordance with the following Regulations;

- Work Health and Safety Act 2011 and Work Health and Safety Regulations 2011
- WorkCover NSW Code of Practice How to manage and control asbestos in the workplace
- Safe Work Australia Code of Practice How to safely remove asbestos
- NSW Work Health and Safety (Hazardous Substances) Regulation 2001
- NSW Work Health and Safety (Asbestos Removal Work) Regulation 2001
- Australian Standard AS2601 [2001] Demolition of Structures
- NSW Protection of the Environment Operations Act [1997]
- NSW Protection of the Environment Operations [Waste] Regulation [2005]
- NSW Office of Environment and Heritage [OEH] Regulations and Guidelines

A Demolition Work Plan must be submitted to WAVERLEY Council and the Principal Certifying Authority (PCA) if WAVERLEY Council is not the PCA, not less than five [5] working days **before commencing any demolition works** involving products or materials "that may" contain asbestos [ACM].

A copy of the Demolition Work Plan must be maintained on site and be made readily accessible to the Council Officer or 'workers' upon request.

ASBESTOS [ACM] REMOVAL CONTROL PLAN

Safe Work Method Statement - Removal & Disposal of Materials that may contain Asbestos

Any work involving the demolition, storage and disposal of products or materials "that may" contain asbestos [ACM] must be carried out as far as is reasonably practicable to minimise the release of airborne asbestos dust and fibres [ACD] in accordance with the following requirements;

- Relevant Work Health and Safety legislation including but not limited to WorkCover NSW Code of Practice How to manage and control asbestos in the workplace; Safe Work Australia Code of Practice How to safely remove asbestos and NSW Office of Environment and Heritage [OEH] requirements.
- The person with Management Control of the workplace and the licensed Asbestos Removalist must, so far as is reasonably practicable, and before commencing the asbestos [ACM] removal work, consult with and inform the following people about the asbestos [ACM] removal work and when the work will commence, so as to eliminate or minimise the exposure of the risks associated with asbestos:
 - The person who commissioned the asbestos removal work [Site Management]
 - A person conducting a business or undertaking at the workplace [Contractors]
 - The occupants of the domestic premises [Owner or Tenant]
 - Anyone occupying premises in the immediate vicinity of the workplace [Neighbours]
- All work procedures are to be devised as far as is reasonably practicable, to minimise the release of dust and fibres [ACD].
- Appropriate warning signage and barricades are to be erected to prevent as far as is reasonably practicable, entry of anyone not connected with the removal activity into the work area.
- The sign must be clearly displayed in a prominent visible position at the front of the site; containing the words "DANGER ASBESTOS REMOVAL IN PROGRESS" and including the details of the licensed Asbestos Removal Contractor [PCBU].
- When working with products and materials "that may" contain asbestos [ACM] all 'workers' are to wear personal protective equipment [PPE] including coveralls and approved respiratory protective equipment [RPE] in accordance with the requirements of AS/NZS1716 Respiratory Protection devices and AS/NZS1715- Selection, use and maintenance of respiratory protective devices.
- As far as is reasonably practicable, use non powered hand tools for the removal of the materials that may contain asbestos [ACM] as these generate much less dust [ACD]. Do not use abrasive cutters and sanders, scrub or water blast the surface of products and materials "that may" contain asbestos [ACM].
- All products and materials "that may" contain asbestos [ACM] are to be kept damp to minimise
 as far as is reasonably practicable the generation of airborne asbestos dust and fibres [ACD].
 Prevent and or contain excess run off water.
- Where it is reasonably practicable work in well ventilated areas.
- Use drop sheets to collect debris of materials that may contain asbestos [ACM]. Dispose of smaller products and materials "that may" contain asbestos [ACM] pieces and collected dust [ACD] in recommended heavy duty plastic bags which are clearly labelled "asbestos waste".
- Wet clean or use approved vacuum cleaning equipment [HEPA] which complies with AS/NZS 603335.2.69 Industrial vacuum cleaners. Household vacuum cleaners must never be used where asbestos [ACM] or [ACD] is or may be present, even if the unit has a HEPA filter.
- Wall cladding and ceiling lining sheets "that may" contain asbestos [ACM] are not to be reused.

- All products and materials "that may" contain asbestos [ACM] or [ACD] are to be stored, transported and disposed of in accordance with the NSW Protection of the Environment Operations Act [1997] and NSW Protection of the Environment Operations [Waste] Regulation [2005]
- All products and materials "that may" contain asbestos [ACM] or [ACD] is to be either wrapped
 in recommended heavy duty plastic sheeting or placed in leak proof lined bins or vehicles and
 appropriately covered and sealed.
- All products and materials "that may" contain asbestos [ACM] or [ACD] are to be stored in a secure area and removed from site as soon as is reasonably practicable in a covered leak proof vehicle.
- A Clearance Certificate of Statement, prepared by a suitably competent person i.e. an Occupational Hygienist, WorkCover NSW licensed Asbestos Removalist, licensed Asbestos Assessor or a "competent person" must be provided to Council upon completion of the works prior to an Occupation Certificate being issued, which confirms that the material "that may" contain asbestos [ACM] or [ACD] has been removed appropriately and the relevant Conditions of Consent have been satisfied.
- All products and materials "that may" contain asbestos [ACM] or [ACD] are to be disposed of as soon as is reasonably practicable, at a licensed asbestos disposal site and in a manner approved by WorkCover NSW, NSW Office of Environment and Heritage [OEH] or WAVERLEY Council.

Safe Work Method Statement – Lead based Paints

All Contractors [PCBU's] and 'workers' involved in the cleaning, repairing or replacement of suspected lead based paint are to follow the following procedures in order to minimise as far as is reasonably practicable, health risks from lead based paints. These procedures include but are not limited to:

- Appropriate warning signage and barricades are to be erected to prevent as far as is reasonably practicable, entry of anyone not connected with the removal activity into the work area
- When working with lead based paints all 'workers' are to wear personal protective equipment [PPE] including coveralls and an approved respiratory protective equipment [RPE] in accordance with the requirements of AS/NZS1716 Respiratory Protection devices and AS/NZS1715 Selection, use and maintenance of respiratory protective devices. Eye protection, complying with AS/NZS1336 and AS/NZS1337 whenever full face respirators are not used.
- The property Owner [Client] is to be advised to clear or cover personal effects in adjoining living spaces as much as is practical.
- Any openings between living areas are to be sealed prior to the commencement of any removal work of lead based paints to prevent as far as is reasonably practicable, dust entering the retained living areas.
- Use approved vacuum cleaning equipment [HEPA] which complies with AS/NZS 603335.2.69
 Industrial vacuum cleaners, to prevent as far as is reasonably practicable, the release of dust that may contain lead while it is being removed. Do not use household vacuum cleaners even if the unit has a HEPA filter.
- Dispose of collected lead based paint dust in sealed approved plastic bags which are clearly labelled.

 All dust containing lead or other contaminants is to be disposed of as far as reasonably practicable in a manner, and at a site, approved by WorkCover NSW, NSW Office of Environment and Heritage [OEH], appropriate disposal Authority or WAVERLEY Council.

4. AREAS NOT ASSESSED

Due to method of construction:

- no access was available to the skillion roof section over the Kitchen / Family room
- no access was available to the underfloor area.

5. UNDETECTED HAZARDOUS MATERIALS

Due to the level of accessibility including the presence of obstructions the overall degree of risk of **undetected** hazardous materials is considered as far as *reasonably practicable* to be:

.ow ✓ Moderate	Moderate to High	High	
----------------	------------------	------	--

CERTIFICATION

This document certifies that the existing residence layout described in this report has been assessed as far as *reasonably practicable* for the inclusion of hazardous materials i.e. materials "that may" contain asbestos [ACM] or [ACD], paints "that may" contain lead, ceiling dusts "that may" contain lead or synthetic mineral fibres [SMF] in the existing structure.

This assessment and report was carried out by: John Spindler

Builders Licence No. 84050C

Signed for and on behalf of JONSPIN Building Services Pty. Limited

John Spindler

Date of Issue: 12th December 2014
